Phase 1 — Project Planning

FitHub CRM

Fitness Center Management System — Project Planning Document

Project Phase	Timeline	Platform	Methodology
Phase 1	**4 Weeks**	**Salesforce**	**Agile**

01 Introduction

Why Project Planning Matters

Project planning is the foundation of any successful software development initiative. It defines the direction, allocates resources, and sets measurable goals before a single line of code is written.

The FitHub CRM project aims to digitize and streamline operations for a fitness center using the Salesforce platform. Without structured planning, such a project risks scope creep, missed deadlines, and poor-quality deliverables.

This document outlines the planning phase — covering scope, objectives, methodology, work breakdown, timeline, resources, and risk management — providing a clear roadmap from concept to deployment.

02 Project Scope

IN SCOPE

- Member Management (registration, profiles, status)
- Trainer Management (profiles, assignments)
- Class Management (schedules, capacity)
- Booking System (member class reservations)
- Automation — Email Notifications (confirmations, reminders)
- Reports & Dashboards (attendance, revenue, performance)

OUT OF SCOPE

- Mobile application development
- Payment gateway / billing integration
- Third-party fitness device sync (wearables)
- Multi-branch / franchise management
- Custom Salesforce Lightning component development
- Data migration from legacy systems

03 Project Objectives

O1	Automate the class booking process to eliminate manual scheduling errors and reduce administrative effort by at least 80%.
O2	Centralize member and trainer data within Salesforce, providing a single source of truth for all fitness center records.
O3	Reduce manual administrative work by deploying workflow automation, email alerts, and validation rules.
O4	Improve member experience through timely automated notifications for booking confirmations and class reminders.
O5	Deliver real-time operational visibility via custom Salesforce reports and dashboards for management decision-making.
O6	Ensure data integrity and system reliability through comprehensive testing before deployment.

04 Development Methodology

Agile / Iterative Development Model

The project adopts an Agile methodology, delivering working functionality in short, focused sprints. Each iteration is reviewed, tested, and refined before proceeding to the next phase.

Flexibility	Agile allows requirements to evolve. As CRM features are built and tested in Salesforce, adjustments can be made without disrupting the entire project.
Early Delivery	Working modules (e.g., Member Management) are completed and validated early, reducing end-stage risk.
Continuous Testing	Each sprint includes a testing cycle, ensuring bugs are caught and fixed incrementally rather than accumulated.
Transparency	Regular sprint reviews make progress visible and enable prompt course correction if needed.

05 Work Breakdown Structure (WBS)

Phase 1	Requirement Analysis — Identify functional and non-functional requirements. Define objects, fields, relationships, and automation rules for the Salesforce data model.
Phase 2	System Design — Design the object model (Members, Trainers, Classes, Bookings). Map relationships, define page layouts, and plan automation triggers.

Phase 3	Development — Build Salesforce objects, fields, validation rules, workflow automations, email templates, and record-triggered flows. Configure UI via App Builder.
Phase 4	Testing — Execute unit testing, integration testing, and user acceptance testing (UAT). Validate automation, data integrity, and report accuracy.
Phase 5	Deployment — Move configured components from sandbox to production. Conduct final smoke tests and enable user profiles/permissions.
Phase 6	Documentation — Prepare project report, user manual, and technical documentation suitable for academic submission and stakeholder handover.

06 Timeline & Schedule

Week 1
Requirement Analysis

→

Week 2
Design & Object Creation

→

Week 3
Automation & UI Build

Week 4
Testing, Reports & Deployment

→

Ongoing
Documentation & Review

→

Final
Submission & Handover

07 Resource Planning

Platform
- Salesforce Developer Edition
- CRM & Automation Engine
- Free developer sandbox

Human Resources
- Student Developer (solo)
- Project Manager role (student)
- Academic supervisor guidance

Tools & Access
- Salesforce Setup & App Builder
- Process Builder / Flow Builder
- Salesforce Reports & Dashboard

References
- Salesforce Trailhead (documentation)
- Academic CRM research papers
- Internet & online tutorials

08 Risk Management

Data Integrity Risk	**Risk:** Incorrect or inconsistent member/booking records leading to system errors.	**Mitigation:** Implement Salesforce Validation Rules on all critical fields. Enforce required fields and picklist constraints.
Automation Failure	**Risk:** Workflow or Flow automations may not trigger correctly under all conditions.	**Mitigation:**

		Conduct thorough trigger-based testing in sandbox. Test edge cases before production deployment.
Timeline Delay	**Risk:** Scope expansion or underestimation of Salesforce configuration complexity.	**Mitigation:** Adhere strictly to WBS. Prioritize core features; defer enhancements to post-submission phase.
Knowledge Gap	**Risk:** Unfamiliarity with advanced Salesforce features (e.g., complex flows).	**Mitigation:** Leverage Salesforce Trailhead and documentation. Allocate buffer time in Week 3 for learning.
Scope Creep	**Risk:** Stakeholder requests for features outside the defined scope during development.	**Mitigation:** Reference scope document to evaluate all change requests. Only critical changes accepted formally.

09 Project Flow Diagram

End-to-End Project Lifecycle

The following diagram illustrates the complete project flow from initial planning through to final documentation and submission.

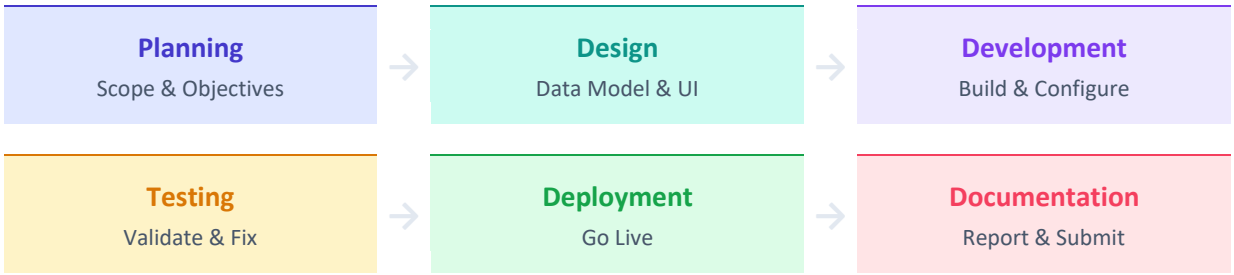

10 Conclusion

Planning as the Cornerstone of Project Success

A well-structured planning phase is not an optional preliminary — it is the strategic backbone that determines whether a CRM project succeeds or fails.

This Project Planning Document for FitHub CRM has established a comprehensive foundation across all critical dimensions: a clearly defined scope prevents wasted effort; measurable objectives provide accountability; an Agile methodology ensures flexibility; a structured WBS makes complex work manageable; and a proactive risk management plan protects the project from foreseeable challenges.

By investing in thorough planning before development begins, the FitHub CRM project is positioned to deliver a fully functional Salesforce-based fitness management system on time, within scope, and to a professional academic standard.

The planning artifacts produced in this phase — scope definition, WBS, timeline, and risk register — will serve as living reference documents throughout development, ensuring that every sprint stays aligned with the project's original vision and academic objectives.

FitHub CRM — Phase 1 Complete

Ready to proceed to Phase 2: System Design & Object Creation
